ML-2

Cheyenne Schedule

Cheyenne Tier 1 Scheulde

11-Oct-11 15:09

Activity ID	Activity Name	Original Duration	Start	Finish
	Cheyenne Schedule	401	01-Nov-12	02-Jun-14
050	Detailed Engineering	380	01-Nov-12*	01-May-14
010	Issue Air Permit	0		01-Nov-12*
020	Issue CPCN	0		01-Nov-12*
100	Construction	255	01-Apr-13*	01-Apr-14
110	Initial sitew ork	32	01-Apr-13*	15-May-13
120	Piling Complete	19	07-May-13*	31-May-13
130	Civil / Substructure Construction	121	15-May-13*	01-Nov-13
140	Mechanical / Piping Construction	147	15-Aug-13*	14-Mar-14
150	Administration Building Construction	62	03-Sep-13*	27-Nov-13
160	Foundations ready to receive HRSGs	0		03-Sep-13*
170	Foundations ready to receive CTGs	0		03-Sep-13*
190	Receive on site - Combined Cycle HRSGs (2)	0		16-Sep-13*
180	Foundation ready to receive STG	0		01-Oct-13*
200	Receive on site - Combined Cycle CTGs (2)	0		01-Oct-13*
210	Receive on site - Simple Cycle CTG	0		07-Oct-13*
230	Electrical Construction	117	15-Oct-13*	01-Apr-14
220	Receive on site - Combined Cycle STG	0		01-Nov-13*
240	Receive on site - APEs	0		01-Nov-13*
250	Receive on site - Combined Cycle GSU	0		01-Nov-13*
260	Receive on site - Simple Cycle GSU	0		15-Nov-13*
270	Commissioning	107	02-Jan-14*	30-May-14
280	Backfeed Combined Cycle GSU	0		17-Feb-14*
290	Insulation	64	17-Feb-14*	15-May-14
300	Backfeed Simple Cycle GSU	0		03-Mar-14*
310	Combined Cycle Chemical Clean Complete	0		15-Apr-14*
320	First Fire, Close Breaker, Sync to Grid - Combined Cycle CTGs	0		22-Apr-14*
330	First Fire, Close Breaker, Sync to Grid - Simple Cycle CTG	0		01-May-14*
340	Combined Cycle Steam Blow s Complete	0		01-May-14*
350	Combined Cycle STG Hot Commissioning	0		15-May-14*
360	Simple Cycle Performance Testing / Emissions Compliance	0		22-May-14*
370	Combined Cycle Performance Testing / Emissions Compliance	0		22-May-14*
380	Commercial Operation - Simple Cycle	0		02-Jun-14*
390	Commercial Operation - Combined Cycle	0		02-Jun-14*

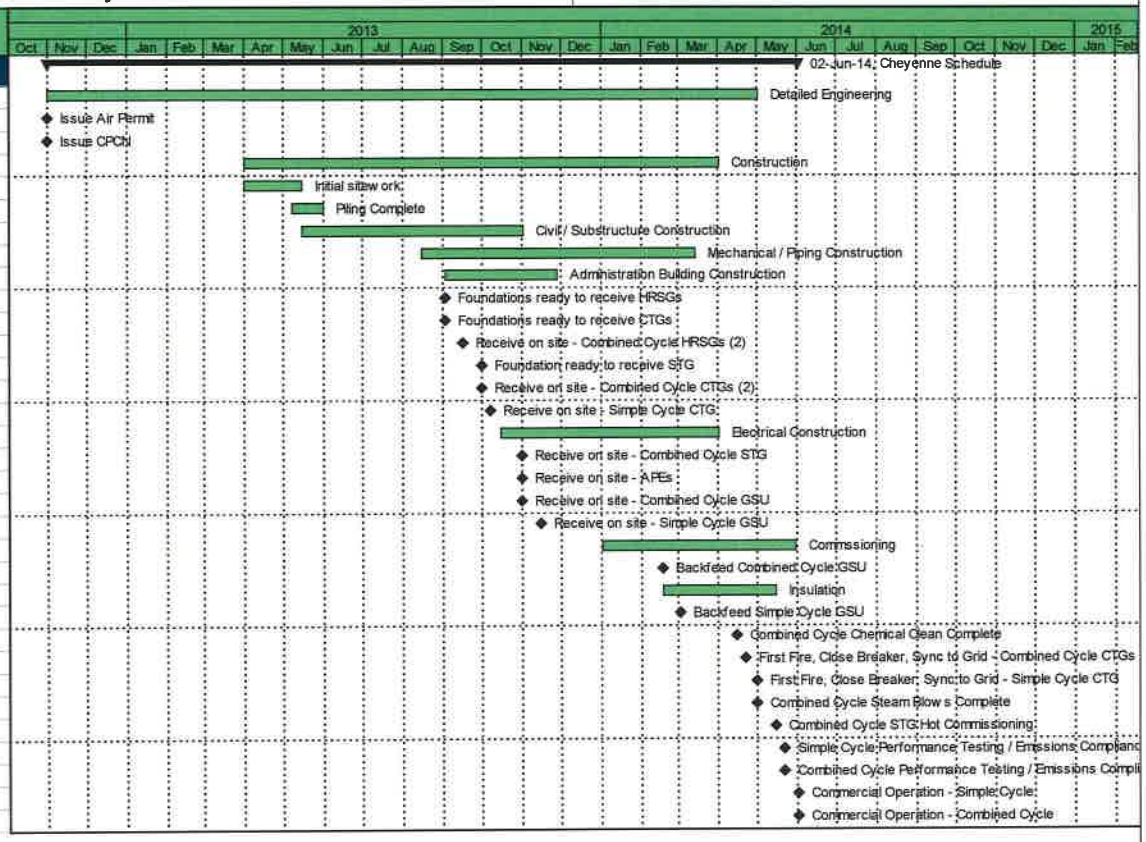

Remaining Level of Effort
Critical Remaining Work
WBS Summary Progress
Actual Level of Effort
Milestone
Actual Work
Summary
Remaining Work
WBS Summary Activity

Date	Revision	Checked	Approved

EXHIBIT

22

tabbies
